



GENERAL TTM NOTES

1. SIGNS AND DEVICES SHALL BE INSTALLED BY A COMPETENT PERSON.
2. SIGNS AND DEVICES SHALL BE APPROPRIATE TO THE CONDITIONS AT THE WORK SITE AND SHALL BE USED IN ACCORDANCE WITH THIS STANDARD UNLESS A RISK ASSESSMENT BY A COMPETENT PERSON INDICATES THAT AN ALTERNATIVE ARRANGEMENT IS SATISFACTORY.
3. SIGNS AND DEVICES SHALL BE ERECTED AND DISPLAYED BEFORE WORK COMMENCES AT A WORK SITE.
4. SIGNS AND DEVICES SHALL BE REGULARLY CHECKED AND MAINTAINED IN A SATISFACTORY CONDITION.
5. SIGNS AND DEVICES SHALL BE REMOVED OR COVERED FROM A WORK SITE AS SOON AS PRACTICABLE.
6. HOWEVER, APPROPRIATE SIGNS SHOULD REMAIN IN PLACE UNTIL ALL WORK HAS BEEN COMPLETED. WHERE WORKS REQUIRE THE RELOCATION OF REGULATORY TRAFFIC CONTROL ITEMS, THEY SHALL BE RELOCATED OR REINSTALLED PROMPTLY IN POSITIONS WHERE THEY ARE VISIBLE AND CAN PERFORM THE REGULATORY FUNCTION.
7. ENSURE TEMPORARY TRAFFIC MANAGEMENT SIGNS DO NOT OBSTRUCT DRIVEWAY LINES OF SIGHT AND ARE VISIBLE TO TRAFFIC.
8. ENSURE TEMPORARY TRAFFIC MANAGEMENT SIGNS DO NOT BLOCK SAFE PEDESTRIAN MOVEMENT ESPECIALLY FOR DISABLED PERSONS.
9. ADDITIONAL TRAFFIC MANAGEMENT PLANS MAY BE REQUIRED DURING THE CONSTRUCTION PHASE OF THE DEVELOPMENT FOR SPECIFIC SITUATIONS. THE PROJECT MANAGER IS TO ARRANGE THE NECESSARY DOCUMENTATION, FEES, PERMITS AND APPROVALS AS REQUIRED.
10. ILLEGALLY PARKED VEHICLES MAY BE FINED.
11. ALL FEES AND PERMITS ARE TO BE PAID PRIOR TO THE RELEASE OF THE APPROVED TEMPORARY TRAFFIC MANAGEMENT PLAN.

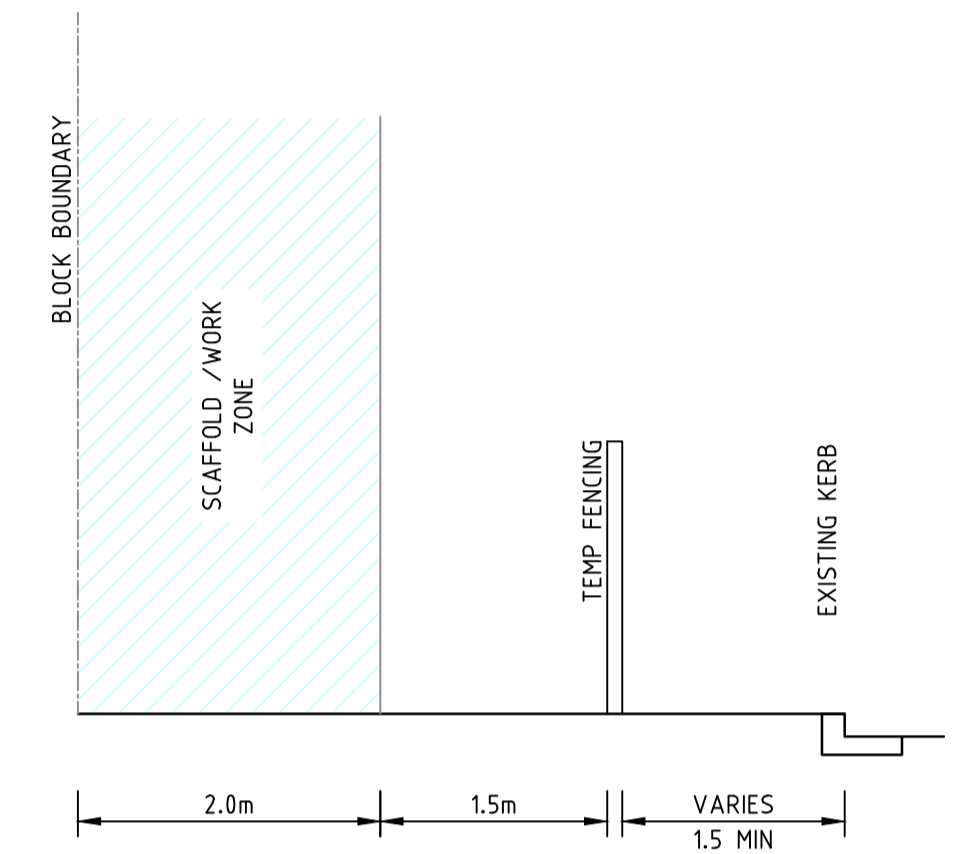

TYPICAL VERGE SECTION

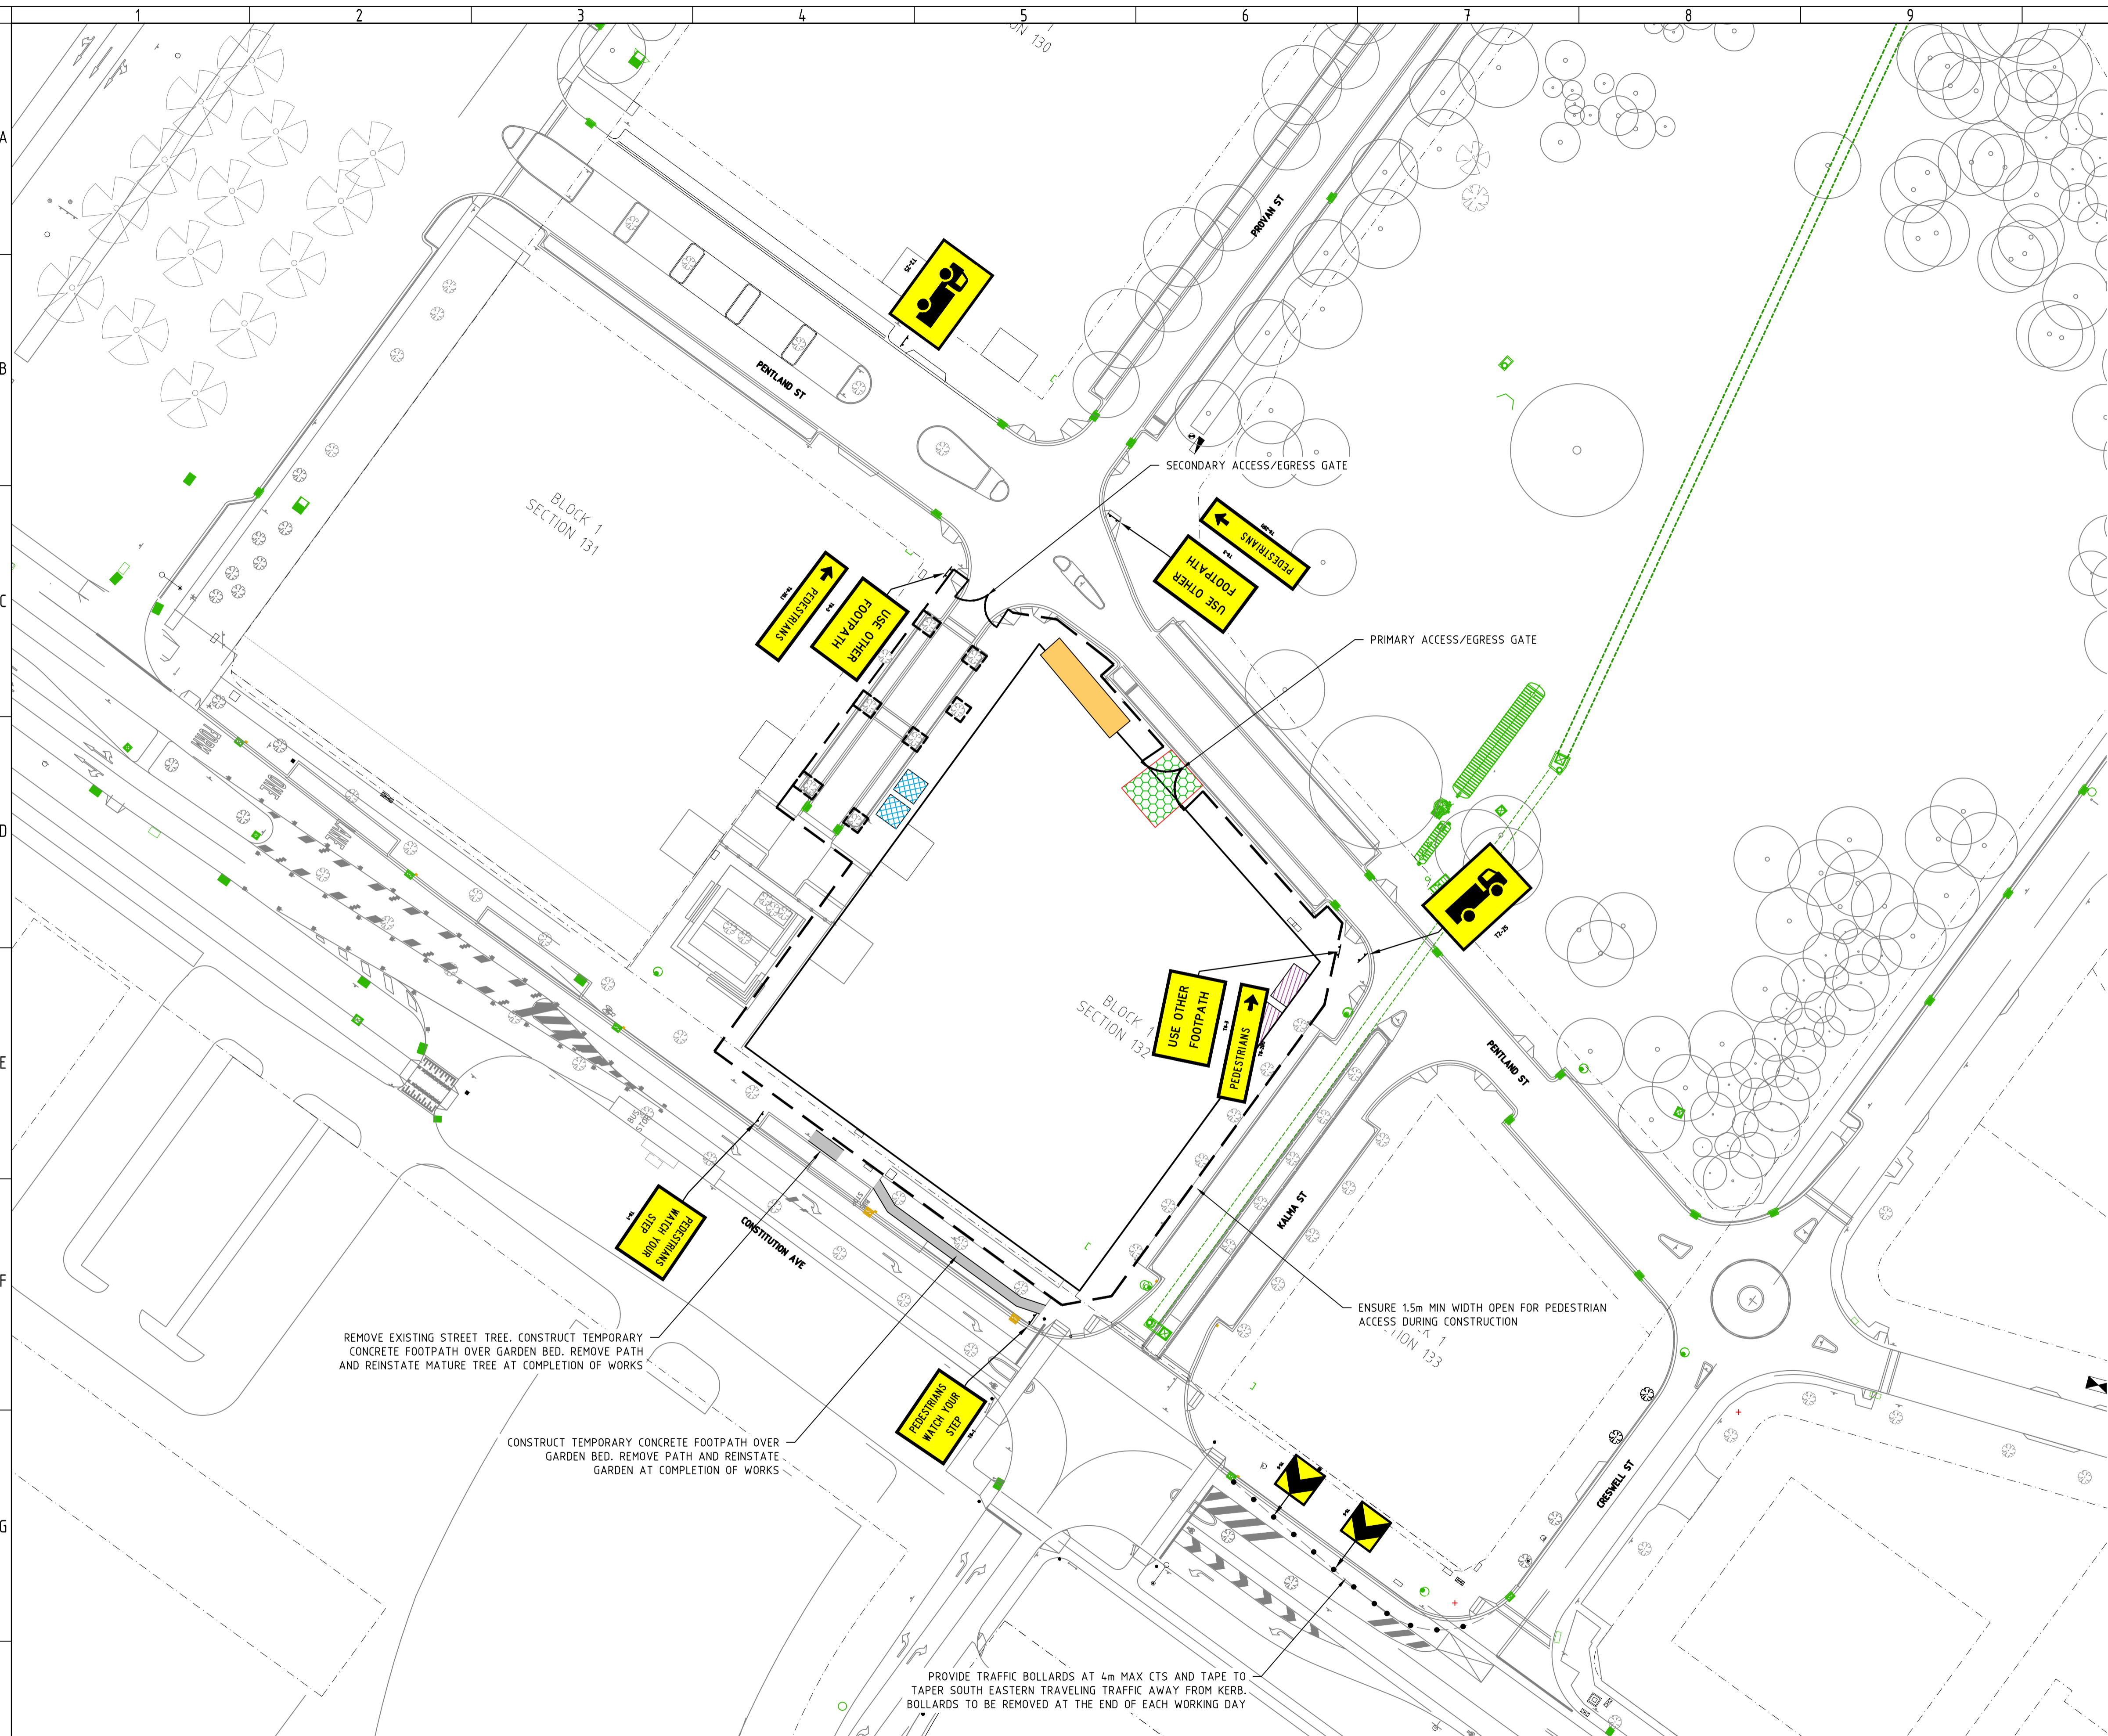

REMOVE EXISTING STREET TREE. CONSTRUCT TEMPORARY CONCRETE FOOTPATH OVER GARDEN BED. REMOVE PATH AND REINSTATE MATURE TREE AT COMPLETION OF WORKS


CONSTRUCT TEMPORARY CONCRETE FOOTPATH OVER GARDEN BED. REMOVE PATH AND REINSTATE GARDEN AT COMPLETION OF WORKS

PEDESTRIANS WITH TOILET STOP

PROVIDE TRAFFIC BOLLARDS AT 4m MAX CTS AND TAPE TO TAPER SOUTH EASTERN TRAVELING TRAFFIC AWAY FROM KERB. BOLLARDS TO BE REMOVED AT THE END OF EACH WORKING DAY

ENSURE 1.5m MIN WIDTH OPEN FOR PEDESTRIAN ACCESS DURING CONSTRUCTION

ISSUE	DESCRIPTION	DATE	DRAWN
1	FOR ROADS ACT APPROVAL	15.11.16	LT
2	FOR DESIGN ACCEPTANCE	20.06.16	AM
3	REVISED FOR WORKS APPROVAL	29.04.16	AM
4	FOR WORKS APPROVAL	28.04.16	AM
5	FOR REVIEW	18.04.16	AM



CLIENT
CHASE

ARCHITECT
FRONT ARCHITECTS

sellick consultants
STRUCTURAL CIVIL HYDRAULIC
canberra | sydney | brisbane
02 6201 0200 www.sellickconsultants.com.au

PROJECT TITLE
**MIXED USE DEVELOPMENT
CAMPBELL 5 - KOBEN**

DO NOT SCALE OFF DRAWINGS
VERIFY ALL DIMENSIONS ON SITE BEFORE COMMENCING WORK
COPYRIGHT: The concepts and information contained in this document are copyright of Sellick Consultants. Use or copying of this document in whole or in part without written permission constitutes an infringement of copyright.

DESIGNED BY
AM

CHECKED BY
CO

AUTHORISED BY

DATE
15/11/2016

DRAWING TITLE
**TEMPORARY TRAFFIC
MANAGEMENT PLAN 1**

PROJECT LOCATION
**BLOCK 1 SECTION 132
CAMPBELL, ACT**

SCALE 0m 5 10 15 20 25 1:500 @A1 1:1000 @A3		
JOB NO. 140779	DRAWING NO. C104	REV. E

NOTE:
THIS TTM IS FOR STAGE 1 (BULK EATH WORKS) ONLY. REFER DRAWING C105 FOR STAGE 2 (CONSTRUCTION WORKS)
